

# Shri Amarnathji Shrine Board



## **Jammu and Kashmir**

### **Notice Inviting Tender**

**Fabrication, Supply and Installation of Structures  
along Baltal Axis  
(Yatra – 2021)**

Sd/-  
**General Manager (Work)**  
Shri Amarnathji Shrine Board

Dated: 15.03.2021

**TENDER FOR THE WORK FABRICATION, SUPPLY AND INSTALLATION OF  
STRUCTURES ALONG BALTAL AXIS  
(YATRA – 2021)**

**DETAILED NOTICE INVITING TENDER (DNIT)**

(issued under no. SASB/NIT/W/2021/121288/22 dated 15.03.2021)

<b>#</b>	<b>CONTENT</b>	<b>PAGE(S)</b>
1	Notice Inviting Tender (NIT) for advertisement	3-4
2	Eligibility criteria	5
3	Documents establishing Bidder's eligibility	5
4	Instructions to Bidders	5-8
5	Terms and Conditions of Contract	9-17
6	Schedule – A (Technical Bid)	18-19
7	Bid Security Declaration Form	20
8	Schedule – B (Financial Bid)	21-38
9	Drawings	39-51



## SHRI AMARNATHJI SHRINE BOARD

(Established under an Act of J&K State Legislature)

Chaitanya Ashram, Talab Tillo, Jammu (Nov-April)

Tele: 0191-2569910, Telefax: 0191-2503399

E-mail sasbik2001@gmail.com

### NOTICE INVITING TENDERS

#### **FABRICATION, SUPPLY AND INSTALLATION OF STRUCTURES ALONG BALTAL AXIS FOR YATRA-2021**

For and on behalf of Chairman, Shri Amarnathji Shrine Board, sealed tenders in two-bid format are invited from reputed and experienced **SSI Unit holders / Micro Small & Medium Entrepreneurs** having valid Registration from District Industries Centre, for the below mentioned works. The Bids shall be received in the Office of General Manager (Works), Shri Amarnathji Shrine Board, Chaitanya Ashram, Talab Tillo, Jammu **on or before 05.04.2021 upto 1400 hours.**

S. No.	Name of work	Approx. Amount (Rs. In Lakhs)	Cost of Tender Document (in Rs)	Earnest Money/ Bid Security (in Rs)	Last date for submission of Tenders
1.	Fabrication, Supply, Carriage and Installation of Mild Steel Frame superstructure of Pandal for Pravachan at Baltal for Yatra-2021. (FoR Baltal)	3.00	300.00	<b>Bid Security Declaration to be made by the bidder in the shape notarized sworn statement on prescribed Format</b>	<b>05.04.2021 upto 1400 hours</b>
2.	Fabrication and supply of Mild Steel racks for shoes(06 Nos.) and for cloak room (02 Nos) at Holy Cave for Yatra-2021. (FoR Baltal)	1.38	100.00		
3.	Fabrication, Supply, Carriage and Installation of super-structure of Control room (size 5.40x2.75 m) with washroom (size 2.00x1.40m) for service providers for issuance of smart card at Dumail for Yatra-2021.	3.20	400.00		
4.	Fabrication, Supply, Carriage and Installation of 01 No. Hut (size 16'-00"x16'-00") with attached washroom and 01 No. kitchen (size 8'-00" x 10'-00") for Heli-services staff at Sangam Top for Yatra-2021.	3.30	400.00		
5.	Fabrication, Supply, Carriage and Installation of super-structure of Double room Camp Director Hut (size 12'-00"x11'-00") with attached washroom (size 6'-00"x4'6") and 01 No. kitchen of size 8'-00"x11'-00" at Sangam Top for Yatra-2021.	3.51	400.00		

S. No.	Name of work	Approx. Amount (Rs. In Lakhs)	Cost of Tender Document (in Rs)	Earnest Money/ Bid Security (in Rs)	Last date for submission of Tenders
6.	Fabrication, Supply, Carriage and Installation of 02 No. Huts (size 16'-00"x16'00") with attached washrooms and 02 No. kitchens (size 8-00"x10'00") for Heli-services staff at Lower Holy-cave for Yatra-2021.	6.62	1000.00	<b>Bid Security Declaration to be made by the bidder in the shape notarized sworn statement on prescribed Format</b>	<b>05.04.2021 upto 1400 hours</b>
7.	Fabrication, Supply, Carriage and Installation of super-structure of Control room ( size 5.40x2.75 m) with washroom (size 2.00x1.40m) for service providers for issuance of smart card to Yatrics and superstructure of Sadhu shed of size 9.75x4.88 m at Lower Holycave for Yatra-2021.	5.68	1000.00		

- DNIT can be obtained from the Office of FA/ Chief Accounts Officer, Shri Amarnathji Shrine Board, (address mentioned above) from **15.03.2021 to 01.04.2021 from 09.30 AM to 5.00 PM** on any working day on payment shown against each work, in cash or in the shape of Demand Draft in favour of FA/ Chief Accounts Officer, Shri Amarnathji Shrine Board (SASB), Jammu. Alternatively, the DNIT can be downloaded from SASB website [www.shriamarnathjishrine.com](http://www.shriamarnathjishrine.com).
- The Tenders, duly completed, along with **Bid Security Declaration** must reach the office of General Manager (Works) latest by **1400 hours** on **05.04.2021**. The bidder, in his own interest, is advised to deliver the bids personally to Chief Accounts Officer, Shri Amarnathji Shrine Board, Chaitanya Ashram, Talab Tillo, Jammu. Alternatively, he may send the same through **Speed Post/ Registered Post**. The Board will not be responsible for any delay, wrong delivery or non-delivery of the bids due to any reasons thereof.
- In case the last date of receipt of bid happens to be a holiday, the bid shall be received on the next working day up to **1400 hours**.
- The Technical bid shall be opened on **05.04.2021 at 1500 hours** in the office of General Manager (Works), (at Jammu Office; address mentioned above) in presence of the bidders who may wish to be present on the occasion.
- All subsequent information/ Corrigendum/ Addendum/ Updates shall be uploaded on **SASB website only**, therefore, the bidders are requested to visit the website regularly for latest updates.
- The successful bidder is bound to enter into an agreement with General Manager (Works), SASB, **within ten days** from the date of the receipt of Letter of Intent.

**No: SASB/NIT/W/2021/1288/22**  
**Dated: 15.03.2021**

**Sd/-**  
**General Manager (Works)**  
**Shri Amarnathji Shrine Board**

## 2. **ELIGIBILITY REQUIREMENT**

- 2.1 The Bidder must be a registered Micro, Small or Medium Enterprise, with Government of Jammu and Kashmir, District Industries Centre.
- 2.2 Consortium or a Joint Venture in any form shall not be eligible for bidding.
- 2.3 Average annual turnover during the last three years, ending 31<sup>st</sup> March of the previous financial year (i.e. 2017-18, 2018-19, 2019-20), should be equal to 30% of the estimated amount of the work.
- 2.4 The Bidder should not have been blacklisted on previous occasion by any of the Central/ Union Territory Government Organizations, Statutory Central/ U.T. Autonomous Bodies, Central/ U.T. Public Sector Undertakings, Central/ U.T. Government owned Hospitals or Local Bodies/ Municipalities.

## 3 **DOCUMENTS ESTABLISHING BIDDER'S ELIGIBILITY**

- 3.1 Registration Certificate from any District Industries Centre of Jammu and Kashmir.
- 3.2 Certified copies of:
  - a) Income tax returns of 2017-18, 2018-19, 2019-20. Bidder shall also submit proof of PAN
  - b) Audited Balance Sheet 2017-18, 2018-19, 2019-20.
  - c) Audited Income and Expenditure Statement 2017-18, 2018-19, 2019-20
- 3.3 Certified copy of PAN Card.
- 3.4 Certified Copy of GSTIN.
- 3.5 General Power of Attorney executed in favour of person authorized to sign the Tender Document and the Contract and all correspondences/ documents thereof.
- 3.6 General information/ Profile of the Bidder.
- 3.7 An affidavit by the Bidder, on Rs. 100 stamp paper, stating that every information furnished in the Tender Document is correct and to the best of his knowledge and that no criminal/ income tax/ blacklisting case is pending against him. If any information is found to be incorrect at any time, the Security Deposit is liable to be forfeited without any notice.

## 4. **INSTRUCTIONS TO BIDDERS:**

Sealed Bids in Two-Bid Format are hereby invited from original Equipment Manufacturers for the Design, Fabrication, Supply and Installation of Sheds at Shrine Board Camps (*for details of these locations, please read Scope of Work*).

- 4.1 Detailed NIT (DNIT) can be obtained from the office of FA/ Chief Accounts Officer, Shri Amarnathji Shrine Board, Chaitanya Ashram, Talab Tillo, Jammu from **15.03.2021 to 01.04.2021** from 0930 Hrs to 1700 Hrs on any working day (Monday to Friday) on payment shown in the DNIT against the work in the shape of Demand Draft in favour of FA/ CAO, Shri Amarnathji Shrine Board (SASB), Jammu. Alternatively, the DNIT can be downloaded from SASB website [www.shriamarnathjishrine.com](http://www.shriamarnathjishrine.com)
- 4.2 The Tenderers are required to submit two separate **Bids** i.e. – **Technical** and **Financial**, as per format given in **Schedule A** and **Schedule B** of the DNIT respectively. The two **Bids** should be submitted in two separately sealed envelopes super-scribed “**Technical Bid for \_\_\_\_\_ Yatra 2021**” and “**Financial Bid for \_\_\_\_\_ Yatra 2021**”. Both the sealed envelopes should be put in a third envelop, sealed and super-scribed “**Tender for Fabrication, Supply and Installation of \_\_\_\_\_ Yatra 2021**”. The bids shall be submitted as per format prescribed in **Schedule A** and **Schedule B** only.
- 4.3 The Tender, duly completed, along with **Bid Security Declaration** must be dropped in the Tender Box kept in the office of General Manager (Works), Shri Amarnathji Shrine Board, Chaitanya Ashram, Talab Tillo, Jammu or sent by Registered Post/ Speed Post to General Manager (Works) at aforesaid address by **1400 hours** on **05.04.2021**. Tenders received after the afore-stated date and time will not be considered. The Shri Amarnathji Shrine Board takes no responsibility for any delay/ loss of documents or correspondence sent by post.
- 4.4 The intending Bidders are advised to obtain information about the actual conditions on ground. The Bidder shall bear all costs associated with the preparation and submission of his bid and the SASB will, in no case, be responsible for those costs, regardless of the conduct or outcome of the bidding process.
- 4.5 The Bidder is expected to examine all Instructions, Schedules, Formats, Terms and Conditions, Scope of Work mentioned in the DNIT. Failure to furnish all relevant information as prescribed in the Tender Document or submission of Tender not substantially responsive to the Tender Document in every respect will be at Bidder’s risk and may result in the rejection of the bid.
- 4.6 All entries in the Technical/ Financial Bids should be legible and should be free from corrections/ erasures/ overwriting/ cuttings. Bids with corrections/ erasures/ overwriting/ cuttings shall be out rightly rejected. Amounts shall be indicated in words as well as in figures. In case of any variation between amount in figures and words, amount quoted in words shall be taken as authentic.
- 4.7 The rate quoted should be inclusive of all taxes including GST as applicable.
- 4.8 The rate quoted by the Contractor in item rate tenders shall be on correct basis and not the amount worked out by them. The rate quoted in words will be correct basis and not the rate shown in figures in case of discrepancy between them.

- 4.9 Any tenderer which stipulates any alteration to any of the conditions laid down or which proposes any other condition of any description whatsoever is liable to be rejected.
- 4.10 The Bidder must satisfy himself that it fulfils all the prescribed eligibility conditions to avoid rejection of its bid.
- 4.11 Each paper of the Tender document shall be completed in all respects, page numbered, and duly signed in long hand, executed in ink and stamped at the bottom right hand corner by an authorized/ empowered representative of the Bidder. The Bidder must also sign and stamp all pages of this DNIT as acceptance of all conditions contained therein and for the purpose of identifications. Financial Bid received in the format other than specified in **Schedule B (Financial Bid)** is liable to be rejected.
- 4.12 Bids must be received at the address specified above not later than the date and time stipulated in this DNIT. The General Manager (Works), SASB may, at his discretion, extend the deadline for submission of bids. Any bid received after the deadline for submission of bids, as stipulated above, shall not be considered and will be returned.
- 4.13 The Bidder shall quote relevant National/ International Code of the parts, along with manufacturer's Name, Trade Mark used in construction.
- 4.14 Clarifications on DNIT, if any, may be sought by the Bidders so as to reach the office of General Manager (Works), SASB at least seven days before last date prescribed for submission of bids. Except for any written clarification by, the General Manager (Works), SASB which is expressly stated to be an addendum to the DNIT, no written or oral communication, presentation or explanation by any other employee of the SASB shall be taken to bind or fetter the Shrine Board under the Contract. All corrigenda, addenda, amendments and clarifications to the DNIT will be hosted on our webpage ([www.shriamarnathjishrine.com](http://www.shriamarnathjishrine.com)) and NOT in the newspaper. Bidders shall keep themselves updated on this account.
- 4.15 The Technical Bid shall be opened at **1500 hours** on **05.04.2021** in the office of the General Manager (Works) Shri Amarnathji Shrine Board, Talab Tillo, Jammu in the presence of the authorized representatives of the firms who may wish to be present at that time. Bidders whose Technical Bids have been accepted shall be informed about the date and time for opening of the Financial Bids.
- 4.16 The General Manager (Works), SASB is not bound to accept the lowest or any bid and may, at any time by notice in writing to the Bidders, terminate the tendering process without assigning any reasons thereof.
- 4.17 The Tender shall remain valid and open for acceptance for a period of 60 days from the last date of receipt of tender.
- 4.18 The General Manager (Works), SASB shall award the Contract to the successful Bidder whose bid has been found to be responsive and who is eligible and qualified to perform the Contract satisfactorily as per Terms and

Conditions incorporated in the DNIT. The General Manager (Works), SASB will communicate the successful Bidder through Registered Post that his bid has been accepted. This letter (hereinafter referred to as the 'Letter of Intent') shall prescribe the amount which the Shrine Board will pay to the Contractor in consideration of work/ services to be executed by the Contractor as prescribed in the Contract.

- 4.19 The eligible Bidder shall be required to furnish a Performance Security Deposit within ten days of receipt of 'Letter of Intent' equal to 5% of the total value of the Contract, in the form of CDR/ FDR in favour of FA & Chief Accounts Officer, SASB. In case the eligible Bidder fails to submit the Performance Security Deposit of the requisite amount within the stipulated period, the 'Letter of Intent' is liable to be withdrawn and the EMD (if deposited) is liable to be forfeited, at the discretion of the Shrine Board.
- 4.20 The eligible Bidder after furnishing the prescribed Performance Security Deposit (PSD) will have to enter into an Agreement with the Shrine Board as per the Terms and Conditions mentioned in the DNIT or such other terms that may be prescribed, within a period of ten days from the date of receipt of 'Letter of Intent'.
- 4.21 General Manager (Works), SASB reserves the right to reject all or any Tender in whole, or in part, without assigning any reasons. Any enquiry after the submission of Bids will not be entertained.

**Sd/-**  
**General Manager (Works)**  
Shri Amarnathji Shrine Board



## **5 Terms and Conditions of Contract:**

- 5.1 **Execution of work:** The Contractor shall complete the work strictly and in accordance with the scope of work given in the DNIT (and as modified in the 'Letter of Award') to the total satisfaction of the Engineer-in-charge i.e. General Manager (Works) or any other Engineer appointed by CEO/ Addl. CEO, SASB). The Contractor must keep in daily contact with Engineer-in-charge to receive instructions regarding work. In the case of an item for which specification are not available in the said Specification, relevant BIS specifications applicable as on the date of Tender shall be followed or, alternatively, the specifications may be decided by the Engineer-In-Charge. Though it is not the intent to specify completely herein all aspects of design and constructional features of a prefab hut and details of work to be carried out, the work shall include all incidental and contingent work which, although not specifically mentioned in Scope of Work, are necessary for completion of work in a sound manner with good workmanship and should be acceptable to the Engineer-in-Charge, who will interpret the meaning of the specifications and drawings and shall have the right to reject or accept any work or material, which in his assessment is not complete to meet the requirements of the specifications and or applicable Standards and Codes mentioned elsewhere in the specifications.
- 5.2 **Role of Engineer-in-charge:** The Engineer-in-charge shall carry out general supervision of the work. The work shall be subject to the approval of Engineer-in-charge from time to time for purposes of determination of the question whether the work is executed by the Contractor in accordance with the contract. He has authority to stop the work, whenever he considers such stoppage necessary to ensure the proper execution of the work. The Engineer-in-charge may issue instructions to the Contractor from time to time during the execution of work for the purpose of proper and adequate executions and maintenance of works and the Contractor shall carry out and be bound by the same. He shall also have authority to inspect and reject all works and materials, which do not conform to the specifications. No claim whatsoever on aforesaid account shall be entertained. In case of any clarification the Contractor may appeal to the General Manager (Works) whose decision shall be final and binding on the Contractor. The above inspection shall, however, not relieve the Contractor of his responsibilities in regard to defective materials or workmanship and the necessity for rectifying or replacing the same.
- 5.3 **Manner of Notice:** Any notice required or permitted by the Contract shall be in English language and may be delivered personally or may be sent by fax/ registered (pre-paid) mail/ email, addressed to the last known address of the Contractor/ Shrine Board.

5.4 **Contractor Superintendence, Supervision, Technical Staff & Employees:**

i. The Contractor shall be solely responsible for the manner and the method of executing the work and provide experienced and qualified supervisors and other manpower for continuous and efficient supervision of works and names, and names of such persons shall be intimated to the Engineer-in-charge during execution of the work and as long thereafter as may be necessary for proper fulfilling the obligations under the Contract. The Engineer-in-charge may direct the Contractor to remove or replace any workman whom he (Engineer-in-charge) considers incompetent or unsuitable. The Engineer-in-charge's opinion as to the competence and suitability of any workmen engaged by the Contractor shall be final and binding on the Contractor.

ii. The agency shall be solely responsible for **Workmen's Compensation Act, 1923** for payment of **compensation to workmen** and their dependants in case of injury and accident (including certain occupational disease) arising out of and in the course of employment and resulting in disablement or death.

5.5 **Information to be supplied by Contractor after award of work:** The Contractor after issue of Letter of Award of work, shall submit within five days of a Time schedule for fabrication, testing, delivery at Chandanwari/ Sheshnag for erection and handing over (completion) for approval of Engineer-in-charge. Any change suggested by Engineer-in-charge shall be incorporated and the work on the contract shall be executed according to the approved schedule as aforesaid. The schedule should be co-related with the date of commencement of Shri Amarnathji Yatra- 2021 (dates to be intimated later). The structures complete in all respects, but in knock-down condition should reach to the site of installation upto 15<sup>th</sup> May, 2021.

5.6 **Commencement of work and completion of drawings:** The Contractor shall be provided with one set of drawings containing details of construction layout, critical sectional details, piping routes along with dimensions with the Tender Document. These drawings shall be;

- a) All general arrangement drawings.
- b) Details along with drawings of various assembled equipment as may be needed generally by Shrine Board for purpose of dismantling/ re-erection/ repair/ modification of structures.

5.7 **Time Extension:** If the Contractor shall desire an extension of the time limit for completion of the work on the grounds of his having been unavoidably hindered in its execution or on any other ground he shall apply in writing to the Engineer-in-Charge within one day of the date of the hindrance on account of which he desires such extensions and Engineer-in-Charge, if in his opinion (which shall be final) reasonable grounds as shown thereof, authorized such extension of time if any, as may, in his opinion be necessary or proper.

## 5.8 **Inspection of Work:**

- (i) All work under or in course of execution or executed in pursuance of the contract shall at all times be open to the inspection and supervision of Engineer-in-charge or his subordinate in-charge of the work.
- (ii) The Contractor shall provide and pay for all necessary tools, instruments gadgets and testing equipments required for conducting various tests. Any defects in material and / or in workmanship detected during initial testing shall be rectified by the Contractor at his own cost. The testing shall be carried out in the presence of Engineer-In-Charge or his representative to his entire satisfaction. The Contractor will produce before the Engineer-in-charge a Test Certificate specifying that the material required for work conforms to ISI standards before it is incorporated in the work.
- (iii) Final inspection will be carried out at the installation site by the Engineer-in-Charge. Whenever preliminary inspection, if any, is carried out at Contractor's works the same shall be subjected to final inspection after complete installation of structures at site (respective sites) and the decision of Engineer-in-charge shall be final.
- (iv) The material rejected by Engineer-in-charge must be removed by Contractor within seven days of rejection, failing which the Board reserves the right to get the rejected material removed at the risk and cost of the Contractor.

5.9 **Guarantee and Defect Liability Period:** The work covered by this contract shall be guaranteed by the contractor against faulty material and workmanship **for a period of 12 months from the date of issue of Completion Certificate** by the Engineer-in-Charge. Any part found defective shall be replaced free of all costs by the Contractor. During the guarantee & defect liability, the Contractor shall provide, at no extra cost, necessary material and personnel to carry out the repairs and routine maintenance of the structures. If performance of assigned work during guarantee period is not found satisfactory, the guarantee period will be extended till satisfactory performance is established for further period of reasonable time decided by competent authority of SASB. The services of the contractor's personnel, if requisitioned during the defect liability period, shall be made available free of any cost to SASB. If the defects noticed during the guarantee period are not removed within a reasonable time SASB shall have the right to restore/rectify the defects at the contractor's risk & cost.

5.10 **Performance Guarantee:** (i) The work shall be executed according to the schedule approved by Engineer-in-charge. Delay in completion of job for a max period of 5 days shall attract a penalty @ 2% of Contract value. After 5 days delay, the General Manager (Works) reserves the right to get the work completed through alternate agency at the risk and cost of the Contractor. The CEO/ Addl. CEO, SASB, on a representation from the Contractor may

reduce the amount of penalty and the decision of the competent authority shall be final and binding.

- (ii) In the event of any loss being caused to the Shrine Board as a result of any lapse on the part of Contractor or personnel engaged by him, duly established after an enquiry conducted by the SASB, the said loss will be recovered from the Contractor upto twice the value of the loss. In such matters, the decision of CEO, SASB shall be final and binding on the Contractor.
  - (iii) If it shall appear to Engineer-in-charge, that any part of work has not been executed or executed with unsound, imperfect or unskilful workmanship or with materials of any inferior description or that any materials or articles provided by him for the execution of the work are unsound or of a quality inferior to the contracted for, or otherwise not in accordance with the contract specifications, the Contractor shall, on demand in writing from the Engineer-in-charge specifying the work materials, articles complained or not withstanding that the same have been inadvertently passed, certified and paid for, forthwith rectify or remove and reconstruct the work so specified in whole or in part as the case may require, or as the case, remove the materials or articles so specified and provide other and suitable materials or articles so specified at his own cost and in the event of his failing to do so within a period to be specified by the Engineer-in-charge, then the Contractor shall be liable to pay compensation at the rate of 1% on the amount of the estimate for every day not exceeding ten days and after completion of ten days the Engineer-in-Charge may rectify or remove, and re-execute the work or remove and replace with other materials or articles complained of, as the case may be at the risk and expenses in all respects of the Contractor. The Engineer-in-charge may reduce the rates at which payments are to be made if the quality of work, although acceptable, is not upto required standard, set forth in the DNIT (as modified by Letter of Award).
  - (iv) Any deviation/ non-compliance with conditions prescribed in the contract shall invoke penalty as decided by CEO/ Addl. CEO, SASB.
- 5.11 **On-Site Support during erection of structures:** As a part of the support, the Contractor will provide qualified engineers and other works to execute the aforesaid works.
- 5.12 **Conformity with Statutory Acts, Rules, Standards and Codes:** The construction and installation shall be carried out in conformity with applicable Acts, Rules, Standards and Codes. Adherence of compliance shall be the sole responsibility of the Contractor to the above Acts, Rules, Standards and Codes applicable in Jammu and Kashmir to the said work.

- 5.13 **Safety codes and regulations:** The contractor shall at his own expenses arrange for the safety provisions as per statutory regulations wherever applicable.
- 5.14 **Provision of utilities / tools etc:** Power supply, water supply and other utilities, if required, at site of work during execution under this Contract shall be arranged by the Contractor at his own cost. The contractor shall be responsible for supply and transportation of water to work site in required quantities both for construction works and drinking purpose of his workers. The contractor shall be responsible for provision and transport of adequate and right type of tools/ accessories, manpower etc in time for efficient execution of work and as may be suggested by Engineer-in-Charge in this regard.
- 5.15 **Storage of materials and safe custody:** The contractor shall be responsible for watch & ward and safe custody of his equipment and installation till they are formally taken over by SASB. Non-availability of lockable storage space due to any reasons shall not relieve the contractor of his contractual obligations in any manner.
- 5.16 **Liability:**
- i) Except as otherwise expressly provided, neither the Board nor its employees, agents or nominees, shall have any liability or responsibility whatsoever to whomsoever (including the owner) for loss or damage to the equipment and or loss or damage to the property of Contractor .
  - ii) Neither the Board nor its employees, agents, nominees, assignees, shall have any liability or responsibility whatsoever for injury to, illness, or death of any employee of the Contractor irrespective of how such injury, illness or death is caused.
- 5.17 **Patents and other Industrial Property Rights:** The prices stated in the present Contract shall be deemed to include all amounts payable for the use of patents, copyrights, registered charges, trademarks and payments for any other industrial property rights. The seller shall indemnify the buyer against all claims from a third party at any time on account of the infringement of any or all the rights mentioned in the previous paragraphs, whether such claims arise in respect of manufacture or use. The seller shall be responsible for the completion of the supplies including spares, tools, technical literature and training aggregates irrespective of the fact of infringement of the supplies, irrespective of the fact of infringement of any or all the rights mentioned above.

5.18 **Terms of payment:** Contractor is to submit the bills in triplicate along with delivery challans to the Engineer-in-charge for works executed by him duly certified by the Engineer-in-charge. 90% Payment to the agency shall be made after supply and assembling/ erection at the respective site and the balance 10% shall be made;

- a) 5% of the contract Value after completion of warranty period of one year.
- b) 5% of the contract Value after on-site support as per clause 5.11 is satisfactorily provided by the Contractor.

5.19 The Contractor shall have no claim against the Shrine Board in respect of any work which may be withdrawn, but only for work actually completed under this contract. The SASB reserves the right to cancel the Agreement at any time upon full payment of work done and the value of the materials collected by the Contractor for permanent incorporation in the work under this Contract upto the date of cancellation of the Contract. The valuation of the work done and the materials collected shall be estimated by the Board's Engineer in the presence of the Contractor. The Contractor shall have no claim to any further payment whatsoever. The valuation would be carried out ex-party if Contractor fails to turn up despite reasonable notice, which will be binding on the Contractor.

5.20 **Contractor to be liable for all taxes / statutory levies:** The rates specified in the tender shall be for finished work including installation at site and inclusive of all taxes as applicable.

5.21. **Income Tax and GSTIN:** i) Deduction on account of Income Tax, GST any other tax in vogue shall be made at the rate prescribed by the relevant authority from time to time from the gross payments due to the contractor in accordance with the statutory provisions.

5.22 **Termination and Consequences thereof:**

- i) The Contract shall be deemed to be automatically terminated on the expiry of duration of the Contract (or extension), if any, thereof.
- ii) In the event that the Contractor at any time during the term of the Contract, becomes insolvent or makes a voluntary assignment of its assets for the benefit of creditors or is adjudged bankrupt, then the Company shall, by a notice in writing have the right to terminate the Contract and all the Contractor's rights and privileges hereunder, shall stand terminated forthwith.
- iii) If the SASB considers that, the performance of the Contractor is unsatisfactory, or not upto the expected standard, the SASB shall notify the Contractor in writing and specify in details the cause of the dissatisfaction. The Board shall have the option to terminate the Contract by giving seven (07) days notice in writing to the Contractor, if the Contractor fails to comply with the requisitions contained in the said written notice issued by the Board.

- iv) In case the Contractor's rights and/ or obligations under the Contract and/ or the Contractor's rights, title and interest to the equipment/ material, are transferred or assigned without the Board's consent, the Board may at its absolute discretion, terminate the Contract.

**5.23 Consequences of Termination:**

- (i) In all cases of termination herein set forth, the relative obligations of the parties to the Contract shall be limited to the period upto the date of termination. Notwithstanding the termination of the Contract, the parties shall continue to be bound by the provisions of the Contract that reasonably require some action or forbearance after such termination.
- (ii) If at any time during the term of the Contract, breakdown of Contractor's equipment results in Contractor's being unable to perform their obligation hereunder for a period of 7 successive days (not including Force Majeure delay), the Board at its opinion, may terminate the Contract in its entirety without any further right or obligation on the part of the Company, except for the payment of money then due. No notice shall be served by the Board under the condition stated above.
- (iii) Upon termination of the Contract, Contractor shall return to the Board all of the Board's assets, which are in Contractor's possession at the time.
- (iv) Notwithstanding any provisions herein to the contrary, the Contract may be terminated at any time by the Board on giving 7 (seven) days written notice to the Contractor and in the event of such termination, the Board shall not be liable to pay any cost or damage to the Contractor except for payment for service charges and other charges as per the Contract upto the date of termination.
- (v) In the event of termination of Contract, the Board will issue Notice of Termination to the Contractor with date or event after which the Contract will be terminated. The Contract shall then stand terminated and the Contractor shall demobilize their personnel and materials.

- 5.24 Force Majeure:** If at any time during the currency of the Contract, either party is subject to force majeure, like civil disturbance, riots, strikes, land disputes etc and acts of Gods, which may prevent either party to discharge the obligations as per the Contract, the affected party shall immediately notify the other party about happening of such an event. Neither party by reason of occurrence of such event be entitled to terminate the Contract in respect of performance of their obligations under the Contract. The performance of

obligations under the Contract shall be resumed as soon as practically possible after the event has come to an end or ceased to exist.

- 5.25 **Arbitration:** Except where otherwise provided in the contract, all questions and disputes relating to the meaning of the specifications, designs, drawings and instructions here in before mentioned and as to the quality of workmanship or materials used on the work or as to any other question, claim, right, matter or thing whatsoever, in any arising out of or relating to the contract, designs, drawings, specifications, estimates, instructions, orders or these conditions or otherwise concerning the works, or the execution or failure to execute the same whether arising during the progress of the work or after the completion or abandonment thereof shall be resolved through joint discussions between CEO, SASB, or his representative and the Contractor. However, in the event of disputes not being resolved by joint discussions, the matter will be referred to a sole Arbitrator to be nominated by the Chairman, Shri Amarnathji Shrine Board (His Excellency the Lt. Governor, J&K), whose decision shall be final and binding on all the parties. The cost of Arbitration shall be borne by the respective parties in equal proportions. During the pendency of the arbitration proceedings and currency of Contract, neither party shall be entitled to suspend the work/ service to which the dispute relates or any other obligation under the Contract on account of arbitration and payment shall continue to be made as per terms of the Contract. The arbitration proceedings will be held at Srinagar only. It is also a term of this contract that no person other than a person appointed by the Chairman, SASB as aforesaid shall act as arbitrator. In all cases where the amount of the claim in dispute is Rs.50000/- (Rs. Fifty thousand only) or above, the arbitrator shall give reasons for the award. It is also a term of the contract that while invoking arbitration the party invoking arbitration shall specify the dispute or disputes to be referred to arbitration under this clause together with the amount or amounts claimed in respect of each such dispute. It is also a term of the contract that if a party does not make any demand for arbitration in respect of any claim(s) in writing within 90 days of receiving the intimation from the Engineer-in-charge that the bill is ready for payment, the claim if any, shall be deemed to have been waived and absolutely barred and the owner shall be discharged and released of all liabilities under the contract in respect of these claims. The arbitration proceedings shall be governed by the provisions of the J&K Conciliation and Arbitration Act, 1997, as amended from time to time.



- 5.26 **Jurisdiction:** Notwithstanding any other courts having jurisdiction to decide the questions forming subject matter of a suit any and all actions and proceedings arising out of or relative to this contract (including any arbitration in terms thereof) shall lie only in the court of competent Civil jurisdiction in this behalf at Jammu and Kashmir, where this contract is to be signed on behalf of SASB and only the said court shall have jurisdiction to try any such actions and/or proceedings to the exclusion of all other courts.

Sd/-  
**General Manager (Works)**  
Shri Amarnathji Shrine Board

**SCHEDULE – A (TECHNICAL BID)****Part – A (Basic Details)**

S. No.	Item	Details
1	Name of Work	
2	Name of Agency	
3	Legal Status of the Agency (whether a Company/ Firm)	
4	Address of the Agency (along with phone and email ID)	
5	Name, Address, Phone numbers (Landline and Mobile) and email ID of the authorized person of the Agency with whom to deal	<div>Name:</div> <div>Address:</div> <div>Phone:</div> <div>Email:</div>
6	PAN No. (please enclose an attested copy)	
7	GSTIN. (please enclose an attested copy)	
8	Details of Banker and Bank Account No.	
9	Availability of credit facility duly certified by the Bankers <i>(not more than three months)</i>	
10	<b>Registration details:</b> Registration No. / other documents of the Agency <i>(attach a certified copy of Registration Certificate/ other documents; please see DNIT – ‘Documents Establishing Bidder’s Eligibility’)</i>	<div>Registration No:</div> <div>Date of Issue:</div> <div>Date of Expiry:</div> <div>Authority with whom registered and their address:</div>

11	Name and address (along with phone numbers and Email) of Directors/ Owners/ Executive Council Members, as applicable <i>(Add separate sheet, if necessary)</i>	S. no.	Name	Address
12	Amount and details of Tender Fee paid	Rs. <i>(in words)</i> :		
		DD No.: Cash Receipt No:		
		Date:		
13	Bid Security Declaration	Dated:		
		Bid No.		
		Date of Notary		
14	Whether General Power of Attorney/ Board of Directors Resolution/ Deed of Authority executed in favour of person(s) authorized to sign the Tender Document, and the Contract, and all correspondence Documents thereof attached <i>(Please attach a certified copy of the relevant documents)</i> (YES/ NO)?			
15	Whether an Affidavit on Rs.100/- Stamp paper stating that every information furnished by the Tenderer is correct and to the best of his knowledge and that no criminal/ income tax/ blacklisting case is pending against him attached (YES/ NO)? <i>(Please attach the affidavit)</i>			

Signature of Bidder  
(with seal)

## **Form of Bid Security Declaration**

(Duly notarized)

**The General Manager (Works),**

\_\_\_\_\_,  
\_\_\_\_\_.

**NIT No. & Date:** \_\_\_\_\_

**Name of work.** \_\_\_\_\_

1. I \_\_\_\_\_ s/o \_\_\_\_\_  
r/o \_\_\_\_\_ declared that;

I understand that, according to your conditions, bids must be supported by a Bid Securing Declaration.

2. I accept that I may be disqualified from any Contract with the Shri Amarnathji Shrine Board for a period of three years from the date of notification if am in a breach of any obligations (s) under the bid conditions, because I;
- a). have withdrawn/ modified/ amended, impaired or derogated from the tender, my bid during the period of bid validity specified in the Letter of Bid, or
  - b). having been notified of the acceptance of my Bid by the SASB during the period of bid validity of (i) fail or refuse to execute the Contract, if required, or (ii) fail or refuse to furnish the Performance Security, in accordance with Instructions to Bidders.
3. I understand this Bid- Securing Declaration shall cease/ expire to be valid if undersigned is not the successful Bidder, upon the earlier of (i) the receipt of your notification of the name of the successful Bidder; or (ii) sixty days Bid Validity Period.

**Signature of person**

(Signing the Bid Securing Declaration)

Dated on \_\_\_\_\_ day of \_\_\_\_\_

## **SCHEDULE – B (Format for Financial Bid)**

### **Rate List/ Quantity Schedule**

**Name of Work:** Fabrication, Supply, Carriage and Installation of Mild steel frame super-structure of Pandal for Pravachan at Yatra-2021. (FoR Baltal)

**S.No:01**

**Adv. Amount: Rs. 3.00 lakh**

<b>S. No.</b>	<b>Particulars of Items</b>	<b>Approx. Quantity</b>	<b>Unit</b>	<b>Rate to be quoted by the Bidder (in Rs.)</b>	<b>Amount (in Rs. )</b>
<b>I</b>	<b>II</b>	<b>III</b>	<b>IV</b>	<b>VI</b>	<b>VII</b>
1	Steel work in built up tubular (round, square or rectangular hollow tubes etc.) trusses etc., including cutting , hoisting , fixing in position and applying a priming coat of approved steel primer, including welding and bolted with special shaped washers etc. and carriage by mechanical transport upto Baltal. Hot finished welded type tubes <u>Job Description</u> All structure in MS tubular 49.5x49.5x2.90 (Drawing Enclosed)	2970.00	Kg		
<b>Total cost of bid (to be quoted both in figures and words)</b>					

**Any typographical error found in Rate list must be read as per Item of J&K Schedule of Rates 2020.**

**Signature of Bidder**

**Junior Engineer**

**DGM**

## **SCHEDULE – B (Format for Financial Bid)**

### **Rate List/ Quantity Schedule**

**Name of Work:** Fabrication and Supply of Mild Steel Racks for Shoes(06 Nos) & for Room (02 Nos) at Holy Cave for Yatra-2021.(FoR Baltal)

**S.No:02**

**Adv. Amount: Rs. 1.38 lakh**

<b>S. No.</b>	<b>Particulars of Items</b>	<b>Approx. Quantity</b>	<b>Unit</b>	<b>Rate to be quoted by the Bidder (in Rs.)</b>	<b>Amount (in Rs. )</b>
<b>I</b>	<b>II</b>	<b>III</b>	<b>IV</b>	<b>VI</b>	<b>VII</b>
1	Structural steel work in welded built up sections and framed work with 1 mm thick PGI sheet shelves, including cutting, hoisting, fixing in position and applying a priming coat of approved steel primer and two or more coats of epoxy paint on mild steel frame structure all complete .FoR Baltal Frame structure with MS angle 40x40x6mm and 30x30x4 mm (Drawing Enclosed)	1280.00	Kg		
<b>Total cost of bid (to be quoted both in figures and words)</b>					

**Any typographical error found in Rate list must be read as per Item of J&K Schedule of Rates 2020.**

**Signature of Bidder**

**Junior Engineer**

**DGM**

## **SCHEDULE – B (Format for Financial Bid)**

### **Rate List/ Quantity Schedule**

**Name of Work:** Fabrication, Supply, Carriage and Installation of super-structure of Control Room of size 5.40x2.75 m with washroom of size 2.00x1.40 m for Service Providers for issuance of Smart Card at Dumail for Yatra-2021.

**S.No: 03**

**Adv. Amount: Rs.3.20 lakh**

<b>S. No.</b>	<b>Particulars of Items</b>	<b>Approx. Quantity</b>	<b>Unit</b>	<b>Rate to be quoted by the Bidder (in Rs.)</b>	<b>Amount (in Rs. )</b>
<b>I</b>	<b>II</b>	<b>III</b>	<b>IV</b>	<b>V</b>	<b>VI</b>
1	Steel work in built up tubular (round, square or rectangular hollow tubes etc.) trusses etc., including cutting , hoisting , fixing in position and applying a priming coat of approved steel primer, including welding and bolted with special shaped washers etc. complete. Hot finished welded type tubes <u>Job Description</u> a) Columns, Truss , Rafters in MS Tubular 96x48x3.2 mm b) Purlins and Extension Purlins in MS Tubular 66x33x2.9mm	891.00	Kg		
2	Structural steel work in built up sections, trusses and framed work, including cutting, hoisting, fixing in position and applying a priming coat of approved steel primer all complete including cost of nuts & bolts. Welded <u>Job Description</u> All column and gusset plates make with MS plate 6mm thick and cleats with MS Plate 5mm thick. Bottom U-Channel of size 50x50x2mm (Make- JINDAL/TATA/SAIL/JSW)	270.00	Kg		

3	<p>Providing and fixing PUF insulated sandwich panels for walls of total thickness not less than 50 mm &amp; width 1.0 m having tongue and groove edge finish with camlock arrangement . Panel shall have 0.5 mm thick precoated GI sheet on both side of Polyurethane foam confirming to IS 12436: 1988. The precoated sheet shall be of minimum 240 MPa steel grade confirming to Is 14246: 1995 &amp; shall have zinc coating of minimum 120gsm as per IS 277: 1992 , 5-7 microns epoxy primer on both side of sheet and polyester top coat 20 microns. The PPGL sheet should have plastic protective guard film of minimum 25 microns to avoid scratches while transportation . The PU foam shall be self-extinguishing, fire retardant type having minimum density of 40kg/cum (+/- 2kgs) including CFC free panel should be GRIHA certified. The panels shall be fixed to steel frame structure with minimum 5 mm thick self tapping GI screws of required length and numbers with minimum spacing of 300 mm centre to centre. Payment of GI boxes /conduits to be paid separately. (Make- Jindalmectec/E Pack polymers/Modern Prefab systems)</p>	63.65	Sqm		
4	<p>Providing and fixing precoated galvanized iron profile sheets (size, shape and pitch of corrugation as approved by Engineer-in-charge) 0.50 mm (+ 0.05 %) total coated thickness with zinc coating 120 grams per sqm as per IS: 277, in 240 mpa steel grade, 5-7 microns epoxy primer on both side of the sheet and polyester top coat 15-18 microns. Sheet</p>	48.72	Sqm		



	should have protective guard film of 25 microns minimum to avoid scratches during transportation and should be supplied in single length upto 12 metre or as desired by Engineer-in-charge. The sheet shall be fixed using self drilling /self tapping screws of size (5.5x 55 mm) with EPDM seal, complete upto any pitch in horizontal/ vertical or curved surfaces, excluding the cost of purlins, rafters and trusses and including cutting to size and shape wherever required.				
5	<p>Providing and fixing precoated galvanised steel sheet roofing accessories 0.50 mm (+0.05 %) total coated thickness, Zinc coating 120 grams per sqm as per IS: 277, in 240 mpa steel grade, 5-7 microns epoxy primer on both side of the sheet and polyester top coat 15-18 microns using self drilling/ self tapping screws complete :</p> <p>a) Ridges plain (500 - 600mm) 6.00 Rm</p> <p>b) Bird Cover (300 mm) 10.80 Rm</p> <p>c) Flashings/ Aprons.(Upto 200mm) 59.40 Rm</p>				
6	Supply and fixing of 50mm PUF panel (polyurethane foam conforming to IS 12436:1988 and PPGI sheet conforming to IS 14246:2013 for yield strength and IS 277:2018 for zinc coating , sheet shall have 5-7 micron epoxy primer on both sides and polyester top coat of 15-18 micron .Also, sheet shall have guard film of 25 micron to avoid scratches during transportation) doors with frame work of Aluminum anodized channel (profile) of 60mmx40mmx2mm thick including cost of aluminium				

	handles , Aluminium Al-drop, Tower bolts , hinges etc complete.  Window with sliding shutters of poly carbonate glass 5mm thick with frame work of Aluminum anodized channel (profile) of 60mmx40mmx2mm thick and outside fixed with GI mosquito net and complete locking arrangement.				
	(i) Doors (970x2100mm) shutter of PUF panel 50 mm thick	02	No.		
	(ii) Doors(750x2100mm) shutter of PUF panel 50 mm thick	01	No.		
	(iii) Windows (900x900mm)- sliding shutter 02 No.with GI wire mesh fixed on outer side	01	No.		
	(iv) Service Windows (600x750mm)Single leaf comprises from 6mm thick polycarbonate sheet and aluminium mesh on outer side.	04	No.		
	(v) Ventilator (600x450mm)- sliding shutter 02 No.with wire mesh fixed on outer side	01	No.		
7	Carriage of material by MT from Srinagar to Dumail for an avg lead of 100 Kms	2.20	Tonne		
Total cost of bid (to be quoted both in figures and words)					

**Any typographical error found in Rate list must be read as per Item of J&K Schedule of Rates 2020.**

**Signature of Bidder**

**Junior Engineer**

**DGM**

## **SCHEDULE – B (Format for Financial Bid)**

### **Rate List/ Quantity Schedule**

**Name of Work: Fabrication, Supply, Carriage and Installation of 01 No. Hut of size 16'-00" x 16'-00" with attached washroom and 01 No. Kitchen of Size 8'-00" x 10'-00" for Heli-services staff at Sangam Top for Yatra-2021.**

**S.No: 04**

**Adv. Amount: Rs.3.30 lakh**

<b>S. No.</b>	<b>Particulars of Items</b>	<b>Approx. Quantity</b>	<b>Unit</b>	<b>Rate to be quoted by the Bidder (in Rs.)</b>	<b>Amount (in Rs. )</b>
<b>I</b>	<b>II</b>	<b>III</b>	<b>IV</b>	<b>V</b>	<b>VI</b>
1	<p>Steel work in built up tubular (round, square or rectangular hollow tubes etc.) trusses etc., including cutting , hoisting , fixing in position and applying a priming coat of approved steel primer, including welding and bolted with special shaped washers etc. complete. Hot finished welded type tubes <u>Job Description</u> a) Columns, Truss , Rafters in Ms Tubular 66x33x3.2 mm b) Purlins and Horizontal ties in MS Tubular 60x40x2.9 mm</p>	1142.00	Kg		
2	<p>Structural steel work in built up sections, trusses and framed work, including cutting, hoisting, fixing in position and applying a priming coat of approved steel primer all complete including cost of nuts &amp; bolts. Welded <u>Job Description</u> All column and gusset plates make with MS plate 6mm thick and cleats with MS Plate 5mm thick.</p>	175.00	Kg		
3	<p>Providing and fixing precoated galvanized iron profile sheets (size, shape and pitch of corrugation as approved by Engineer-in-charge) 0.50 mm</p>	119.00	Sqm		

	(+ 0.05 %) total coated thickness with zinc coating 120 grams per sqm as per IS: 277, in 240 mpa steel grade, 5-7 microns epoxy primer on both side of the sheet and polyester top coat 15-18 microns. Sheet should have protective guard film of 25 microns minimum to avoid scratches during transportation and should be supplied in single length upto 12 metre or as desired by Engineer-in-charge. The sheet shall be fixed using self drilling /self tapping screws of size (5.5x 55 mm) with EPDM seal, complete upto any pitch in horizontal/ vertical or curved surfaces, excluding the cost of purlins, rafters and trusses and including cutting to size and shape wherever required.				
4	Providing and fixing precoated galvanised steel sheet roofing accessories 0.50 mm (+0.05 %) total coated thickness, Zinc coating 120 grams per sqm as per IS: 277, in 240 mpa steel grade, 5-7 microns epoxy primer on both side of the sheet and polyester top coat 15-18 microns using self drilling/ self tapping screws complete : Ridges plain (500 - 600mm)	5.50	Rm		
5	Providing and fixing PGI sheet 0.5 mm thick (both inner and outer side) door shutter of 35x35x2.6mm tubular section and 3 mm M S gusset plates at junctions and corners with diagonal braces, all necessary fitting (Butt hinges 100 mm – 4 Nos, Tower Bolts 200mm long & 10mm dia -02 Nos, Handles 125mm- 02 Nos , Al-drop- 200mm long and 10mm dia - 01 No) including frames of Tubular section of size 66x33x2.90mm and applying a priming coat of approved steel primer etc complete job a) Door of size	01	No.		

	0.90mx2.10m b) Door of size 0.75mx2.10m	02	No.		
6	Providing and fixing double leaf 6 mm thick polycarbonate sheet window shutter with its frame of size 35x35x2.6mm tubular section and 3 mm M S gusset plates at junctions and corners with diagonal braces, all necessary fitting (Butt hinges 100 mm – 4 Nos, Tower Bolts 150mm long & 10mm dia -04 Nos, Handles 125mm- 02 Nos ,) including frames of Tubular section of size 50x25x2.90mm and applying a priming coat of approved steel primer etc complete job a) Window of size 0.90mx0.90m b) Ventilator of size 0.60mx0.45m	02 01	No. No.		
7	Carriage of material by MT from Srinagar to Dumail for an avg lead of 100 Kms	2.02	Tonne		
8	Carriage of material by head load for a lead of 11 kms from Dumail to Sangam Top. Porters	67	No.		
Total cost of bid (to be quoted both in figures and words)					

Any typographical error found in Rate list must be read as per Item of J&K Schedule of Rates 2020.

Signature of Bidder

Junior Engineer

DGM

## **SCHEDULE – B (Format for Financial Bid)**

### **Rate List/ Quantity Schedule**

**Name of Work: Fabrication, Supply , Carriage and Installation of super-structure of 02 No. rooms of size 12'-00" x 11'-00" with attached washrooms of size 6'-00" x 4'-6" for camp director and 01 No. kitchen of size 8'-00"x11'-00" at Sangam Top for Yatra-2021.**

**S.No: 05**

**Adv. Amount: Rs.3.51 lakh**

<b>S. No.</b>	<b>Particulars of Items</b>	<b>Approx. Quantity</b>	<b>Unit</b>	<b>Rate to be quoted by the Bidder (in Rs.)</b>	<b>Amount (in Rs. )</b>
<b>I</b>	<b>II</b>	<b>III</b>	<b>IV</b>	<b>V</b>	<b>VI</b>
1	<p>Steel work in built up tubular (round, square or rectangular hollow tubes etc.) trusses etc., including cutting , hoisting , fixing in position and applying a priming coat of approved steel primer, including welding and bolted with special shaped washers etc. complete. Hot finished welded type tubes <u>Job Description</u> a) Vertical Posts /Columns 96x48x3.2mm, Rafters and Trusses in MS Tubular 60x60x2.9mm b) Purlins and Horizontal Channels in MS Tubular 60x40x2.9mm</p>	930.00	Kg		
2	<p>Structural steel work in built up sections, trusses and framed work, including cutting, hoisting, fixing in position and applying a priming coat of approved steel primer all complete including cost of nuts &amp; bolts. Welded <u>Job Description</u> All column and gusset plates make with MS plate 6mm thick and cleats with MS Plate 5mm thick.</p>	154.00	Kg		

3	Providing and fixing precoated galvanized iron profile sheets (size, shape and pitch of corrugation as approved by Engineer-in-charge) 0.50 mm (+ 0.05 %) total coated thickness with zinc coating 120 grams per sqm as per IS: 277, in 240 mpa steel grade, 5-7 microns epoxy primer on both side of the sheet and polyester top coat 15-18 microns. Sheet should have protective guard film of 25 microns minimum to avoid scratches during transportation and should be supplied in single length upto 12 metre or as desired by Engineer-in-charge. The sheet shall be fixed using self drilling /self tapping screws of size (5.5x 55 mm) with EPDM seal, complete upto any pitch in horizontal/ vertical or curved surfaces, excluding the cost of purlins, rafters and trusses and including cutting to size and shape wherever required.	139.00	Sqm		
4	Providing and fixing precoated galvanised steel sheet roofing accessories 0.50 mm (+0.05 %) total coated thickness, Zinc coating 120 grams per sqm as per IS: 277, in 240 mpa steel grade, 5-7 microns epoxy primer on both side of the sheet and polyester top coat 15-18 microns using self drilling/ self tapping screws complete : Ridges plain (500 - 600mm)	9.75	Rm		
5	Providing and fixing PGI sheet 0.5 mm thick (both inner and outer side) door shutter of 35x35x2.6mm tubular section and 3 mm M S gusset plates at junctions and corners with diagonal braces, all necessary fitting (Butt hinges 100 mm – 4 Nos, Tower Bolts 200mm long & 10mm dia -02 Nos, Handles 125mm- 02 Nos , Al-drop-200mm long and 10mm dia - 01 No) including frames of				

	Tubular section of size 66x33x2.90mm and applying a priming coat of approved steel primer etc complete job				
	a) Door of size 0.90mx2.10m	02	No.		
	b) Door of size 0.75mx2.10m	03	No.		
6	Providing and fixing double leaf 6 mm thick polycarbonate sheet window shutter with its frame of size 35x35x2.6mm tubular section and 3 mm M S gusset plates at junctions and corners with diagonal braces, all necessary fitting (Butt hinges 100 mm – 4 Nos, Tower Bolts 150mm long & 10mm dia -04 Nos, Handles 125mm- 02 Nos ,) including frames of Tubular section of size 50x25x2.90mm and applying a priming coat of approved steel primer etc complete job				
	a) Window of size 0.90mx0.90m	05	No.		
	b) Ventilator of size 0.60mx0.45m	02	No.		
7	Carriage of material by MT from Srinagar to Dumail for an avg lead of 100 Kms	2.142	Tonne		
8	Carriage of material by head load for a lead of 11 kms from Dumail to Sangam Top. Porters	71	No.		
Total cost of bid (to be quoted both in figures and words)					

Any typographical error found in Rate list must be read as per Item of J&K Schedule of Rates 2020.

Signature of Bidder

Junior Engineer

DGM



## **SCHEDULE – B (Format for Financial Bid)**

### **Rate List/ Quantity Schedule**

**Name of Work: Fabrication, Supply, Carriage and Installation of 02 No. Huts of size 16'-00" x 16'-00" with attached washrooms and 02 No. Kitchens of size 8'-00" x 10'-00" for Heli-services staff at Lower Holy Cave for Yatra-2021.**

**S.No: 06**

**Adv. Amount: Rs. 6.62 lakh**

<b>S. No.</b>	<b>Particulars of Items</b>	<b>Approx. Quantity</b>	<b>Unit</b>	<b>Rate to be quoted by the Bidder (in Rs.)</b>	<b>Amount (in Rs. )</b>
<b>I</b>	<b>II</b>	<b>III</b>	<b>IV</b>	<b>V</b>	<b>VI</b>
1	<p>Steel work in built up tubular (round, square or rectangular hollow tubes etc.) trusses etc., including cutting , hoisting , fixing in position and applying a priming coat of approved steel primer, including welding and bolted with special shaped washers etc. complete. Hot finished welded type tubes <u>Job Description</u> a) Columns 96x48x3.2 mm, Truss , Rafters in Ms Tubular 66x33x3.2 mm b) Purlins and Horizontal ties in MS Tubular 60x40x2.9 mm</p>	2284.00	Kg		
2	<p>Structural steel work in built up sections, trusses and framed work, including cutting, hoisting, fixing in position and applying a priming coat of approved steel primer all complete including cost of nuts &amp; bolts. Welded <u>Job Description</u> All column and gusset plates make with MS plate 6mm thick and cleats with MS Plate 5mm thick.</p>	350.00	Kg		
3	<p>Providing and fixing precoated galvanized iron profile sheets (size, shape and pitch of corrugation as approved by Engineer-in-charge) 0.50 mm</p>	238.00	Sqm		

	(+ 0.05 %) total coated thickness with zinc coating 120 grams per sqm as per IS: 277, in 240 mpa steel grade, 5-7 microns epoxy primer on both side of the sheet and polyester top coat 15-18 microns. Sheet should have protective guard film of 25 microns minimum to avoid scratches during transportation and should be supplied in single length upto 12 metre or as desired by Engineer-in-charge. The sheet shall be fixed using self drilling /self tapping screws of size (5.5x 55 mm) with EPDM seal, complete upto any pitch in horizontal/ vertical or curved surfaces, excluding the cost of purlins, rafters and trusses and including cutting to size and shape wherever required.				
4	Providing and fixing precoated galvanised steel sheet roofing accessories 0.50 mm (+0.05 %) total coated thickness, Zinc coating 120 grams per sqm as per IS: 277, in 240 mpa steel grade, 5-7 microns epoxy primer on both side of the sheet and polyester top coat 15-18 microns using self drilling/ self tapping screws complete : Ridges plain (500 - 600mm)	11.00	Rm		
5	Providing and fixing PGI sheet 0.5 mm thick (both inner and outer side) door shutter of 35x35x2.6mm tubular section and 3 mm M S gusset plates at junctions and corners with diagonal braces, all necessary fitting (Butt hinges 100 mm – 4 Nos, Tower Bolts 200mm long & 10mm dia -02 Nos, Handles 125mm- 02 Nos , Al-drop- 200mm long and 10mm dia - 01 No) including frames of Tubular section of size 66x33x2.90mm and applying a priming coat of approved steel primer etc complete job				

	a) Door of size 0.90mx2.10m	02	No.		
	b) Door of size 0.75mx2.10m	04	No.		
6	Providing and fixing double leaf 6 mm thick polycarbonate sheet window shutter with its frame of size 35x35x2.6mm tubular section and 3 mm M S gusset plates at junctions and corners with diagonal braces, all necessary fitting (Butt hinges 100 mm – 4 Nos, Tower Bolts 150mm long & 10mm dia -04 Nos, Handles 125mm- 02 Nos ,) including frames of Tubular section of size 50x25x2.90mm and applying a priming coat of approved steel primer etc complete job				
	a) Window of size 0.90mx0.90m	04	No.		
	b) Ventilator of size 0.60mx0.45m	02	No.		
7	Carriage of material by MT from Srinagar to Dumail for an avg lead of 100 Kms	4.03	Tonne		
8	Carriage of material by head load for a lead of 12 kms from Dumail to Holy Cave. Porters	134	No.		
Total cost of bid (to be quoted both in figures and words)					

**Any typographical error found in Rate list must be read as per Item of J&K Schedule of Rates 2020.**

**Signature of Bidder**

**Junior Engineer**

**DGM**

## **SCHEDULE – B (Format for Financial Bid)**

### **Rate List/ Quantity Schedule**

**Name of Work:** Fabrication, Supply, Carriage and Installation of super-structure of Control Room of size 5.40x2.75 m with washroom 2.00x1.40 m for Service Providers for issuance of Smart Card to Yatries and superstructure of Sadhu shed of size 9.75x4.88 m at Lower Holy Cave for Yatra-2021.

**S.No:07**

**Adv. Amount: Rs. 5.68 lakh**

<b>S. No.</b>	<b>Particulars of Items</b>	<b>Approx. Quantity</b>	<b>Unit</b>	<b>Rate to be quoted by the Bidder (in Rs.)</b>	<b>Amount (in Rs. )</b>
<b>I</b>	<b>II</b>	<b>III</b>	<b>IV</b>	<b>V</b>	<b>VI</b>
1	<p>Steel work in built up tubular (round, square or rectangular hollow tubes etc.) trusses etc., including cutting , hoisting , fixing in position and applying a priming coat of approved steel primer, including welding and bolted with special shaped washers etc. complete. Hot finished welded type tubes <u>Job Description</u> A. <u>Sadhu Shed</u> a) Columns make with MS Tubular 75x75x3.2 mm b) Truss, Purlins &amp; Horizontal members make with MS Tubular 49.5x49.5x2.9mm B. <u>Control Room</u> a) Columns and Truss make with MS Tubular 66x33x3.6 mm b) Purlins &amp; Horizontal members make with MS Tubular 35x35x4mm</p>	1890.00	Kg		
2	<p>Structural steel work in built up sections, trusses and framed work, including cutting, hoisting, fixing in position and applying a priming coat of approved steel primer all complete including cost of</p>	435.00	Kg		

	<p>nuts &amp; bolts. Welded</p> <p><u>Job Description</u></p> <p>All columns and gusset plates make with MS plate 6mm thick and cleats with MS Plate 5mm thick.</p>				
3	<p>Providing and fixing precoated galvanized iron profile sheets (size, shape and pitch of corrugation as approved by Engineer-in-charge) 0.50 mm (+ 0.05 %) total coated thickness with zinc coating 120 grams per sqm as per IS: 277, in 240 mpa steel grade, 5-7 microns epoxy primer on both side of the sheet and polyester top coat 15-18 microns. Sheet should have protective guard film of 25 microns minimum to avoid scratches during transportation and should be supplied in single length upto 12 metre or as desired by Engineer-in-charge. The sheet shall be fixed using self drilling /self tapping screws of size (5.5x 55 mm) with EPDM seal, complete upto any pitch in horizontal/ vertical or curved surfaces, excluding the cost of purlins, rafters and trusses and including cutting to size and shape wherever required.</p>	203.94	Sqm		
4	<p>Providing and fixing precoated galvanised steel sheet roofing accessories 0.50 mm (+0.05 %) total coated thickness, Zinc coating 120 grams per sqm as per IS: 277, in 240 mpa steel grade, 5-7 microns epoxy primer on both side of the sheet and polyester top coat 15-18 microns using self drilling/ self tapping screws complete :</p> <p>Ridges plain (500 - 600mm)</p>	5.60	Rm		
5	<p>Providing and fixing PGI sheet 0.5 mm thick (both inner and outer side) door shutter of 35x35x2.6mm tubular section and 3 mm M S gusset plates at junctions and corners with diagonal braces, all necessary</p>				

	fitting (Butt hinges 100 mm – 4 Nos, Tower Bolts 200mm long & 10mm dia -02 Nos, Handles 125mm- 02 Nos , Al-drop-200mm long and 10mm dia - 01 No) including frames of Tubular section of size 66x33x2.90mm and applying a priming coat of approved steel primer etc complete job a) Door of size 0.90mx2.10m b) Door of size 0.75mx2.10m	03 01	No. No.		
6	Providing and fixing double leaf 6 mm thick polycarbonate sheet window shutter with its frame of size 35x35x2.6mm tubular section and 3 mm M S gusset plates at junctions and corners with diagonal braces, all necessary fitting (Butt hinges 100 mm – 4 Nos, Tower Bolts 150mm long & 10mm dia -04 Nos, Handles 125mm- 02 Nos ,) including frames of Tubular section of size 50x25x2.90mm and applying a priming coat of approved steel primer etc complete job a) Window of size 0.90mx0.90m b) Ventilator of size 0.60mx0.45m	04 01	No. No.		
7	Carriage of material by MT from Srinagar to Dumail for an avg lead of 100 Kms	3.53	Tonne		
8	Carriage of material by head load for a lead of 11 kms from Dumail to Holy Cave. Porters	117.00	No.		
Total cost of bid (to be quoted both in figures and words)					

Any typographical error found in Rate list must be read as per Item of J&K Schedule of Rates 2020.


Signature of Bidder

Junior Engineer

DGM

# **DRAWINGS**



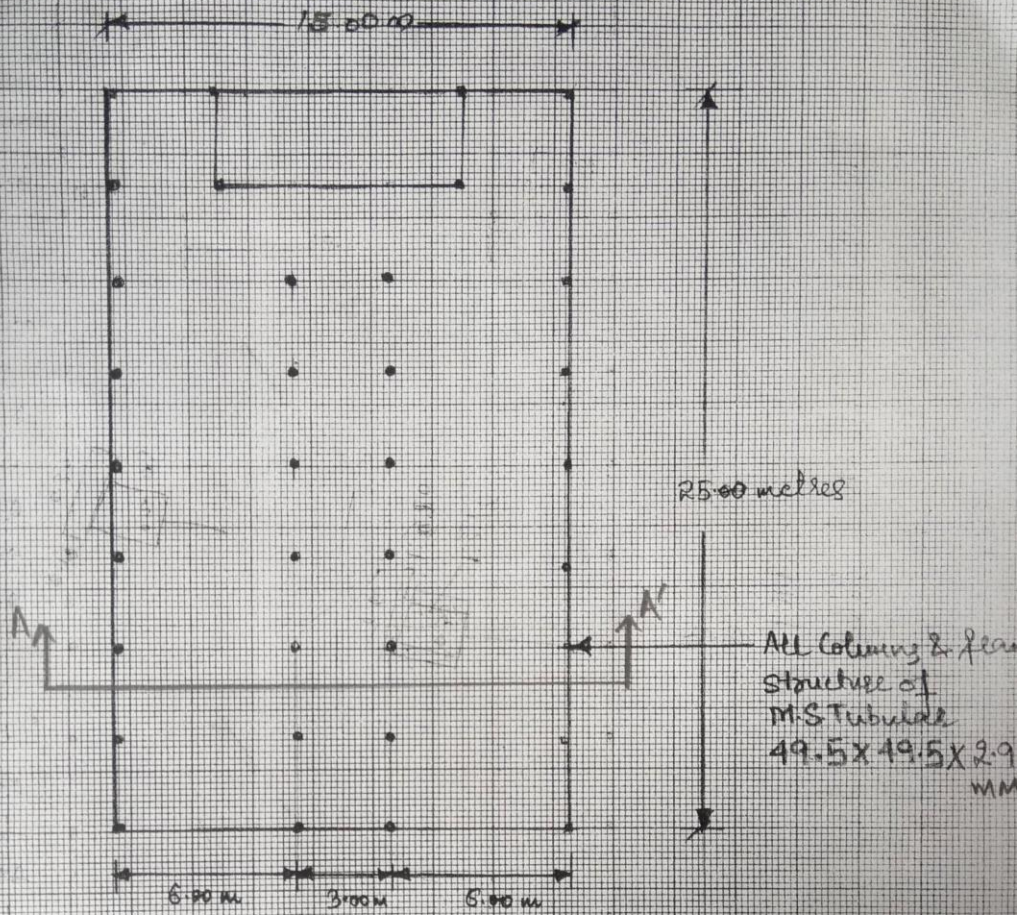


PARVACHAN HALL AT BALTAL  
PLAN (15 X 25 metres)

Optu  
(JE)

Page No. of 102

Teacher's Signature : .....



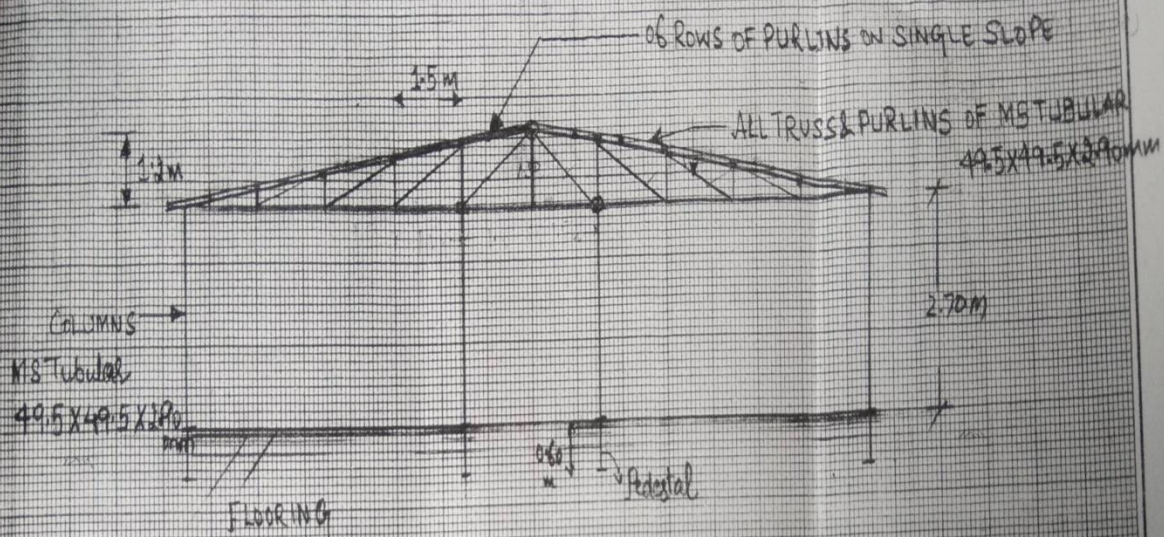

PARVACHAN HALL AT BALTAL

X-SECTION AT A-A'

Page No. of job

Dr. (E)



2.70m = 2.70m x 1.0 = 2.70m

Scale = 1cm = 2m

Scanned by TapScanner




S.No 2nd

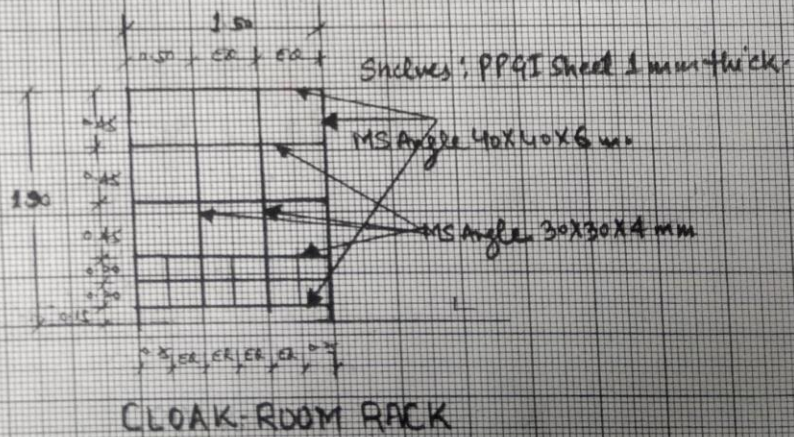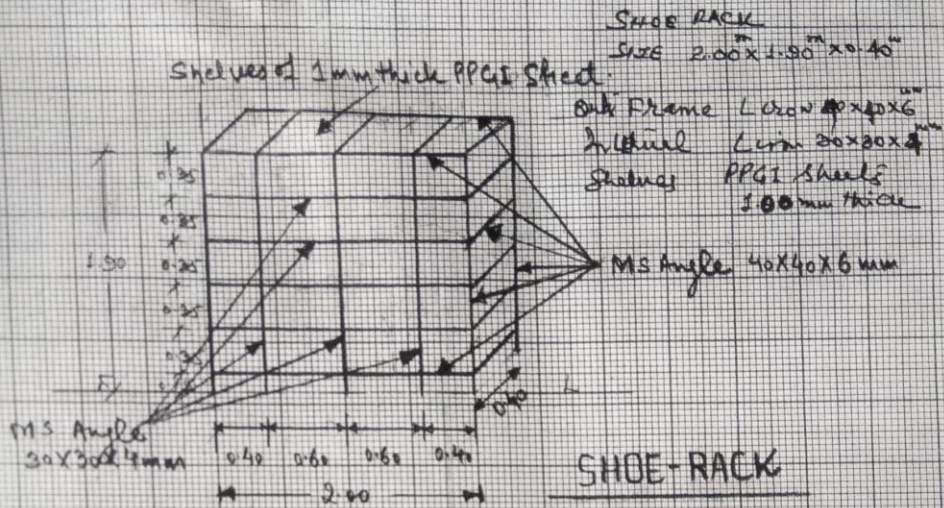

*M. S. Ramesh*  
*(SE)*

*Dr. M. S. Ramesh*

(S.No 394)  
**DETAILED PLAN FOR THE CONSTRUCTION OF OFFICE CUM RESIDENTIAL HUT FOR SERVICE PROVIDERS FOR ISSUANCE OF SMART CARDS (TRACKING) TO YATRIES AT DOMAIL**

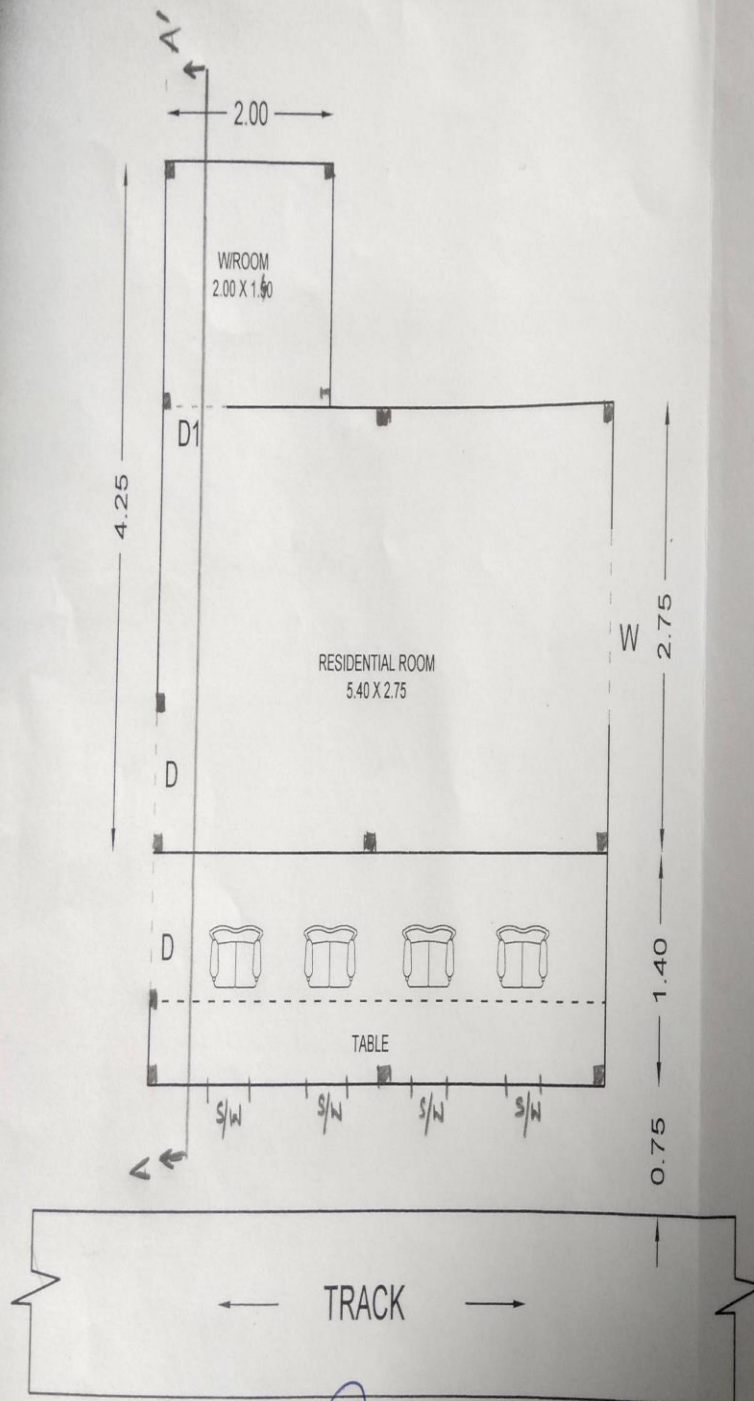

*[Signature]*  
 JE

*[Signature]*  
 (BARTAL)


gm(walus)

ALL DIMENSIONS ARE IN METERS  
 D = 0.90 X 2.10  
 D1 = 0.75 X 2.10  
 W = 1.20 X 1.20


*[Signature]*  
 JE  
*[Signature]*  
 Page No. 01 of 02.



# SMART CARD SERVICE PROVIDERS AT DOMAIL

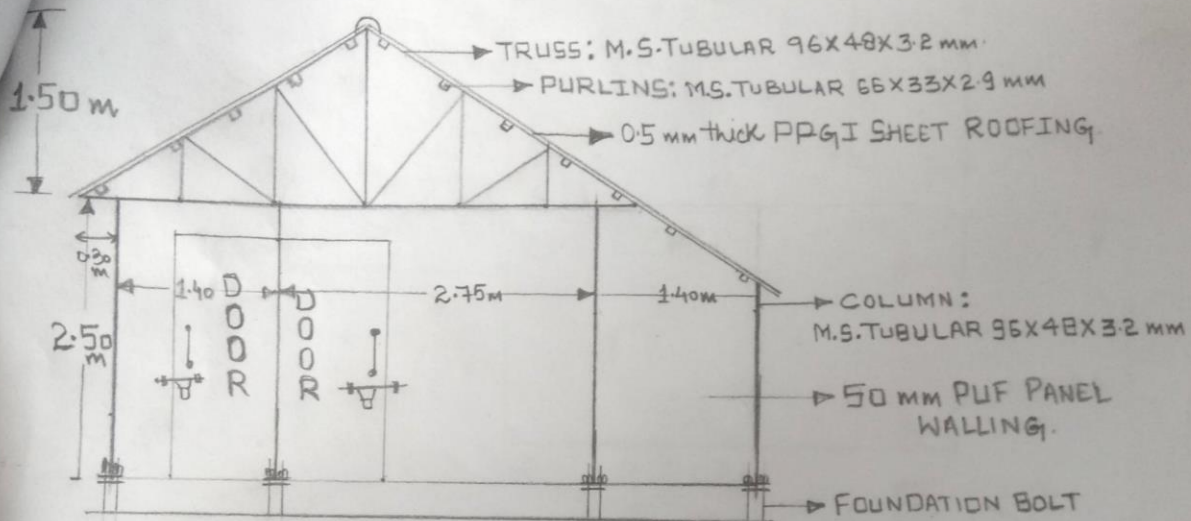

X-SECTION AT A-A'

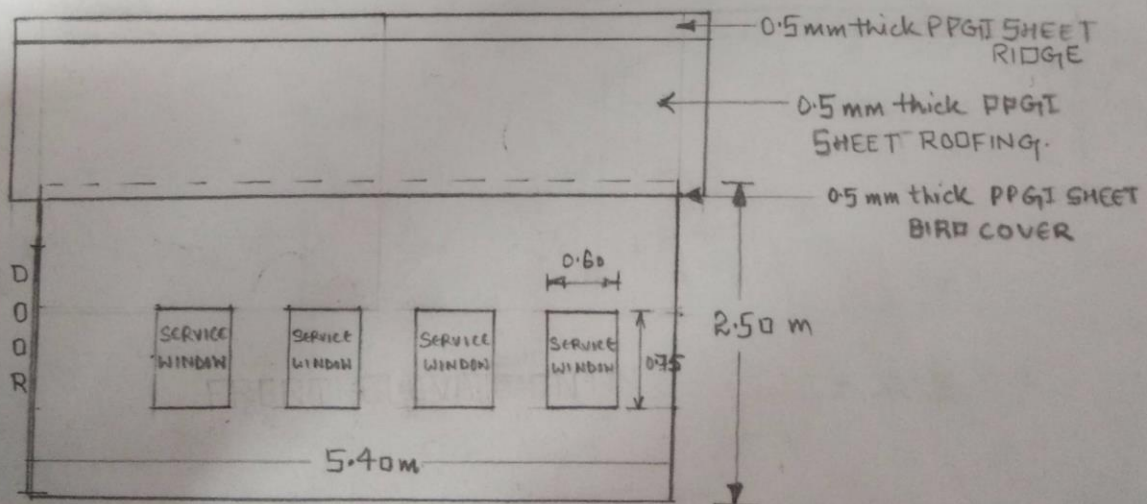

FRONT ELEVATION


*Signature*

Page No 02402


Scanned by TapScanner

# DRAWING S.No 4th HELI-SERVICES SHED AT SANGAM & LOWER HOLY CAV

MAP NOT-TO-SCALE

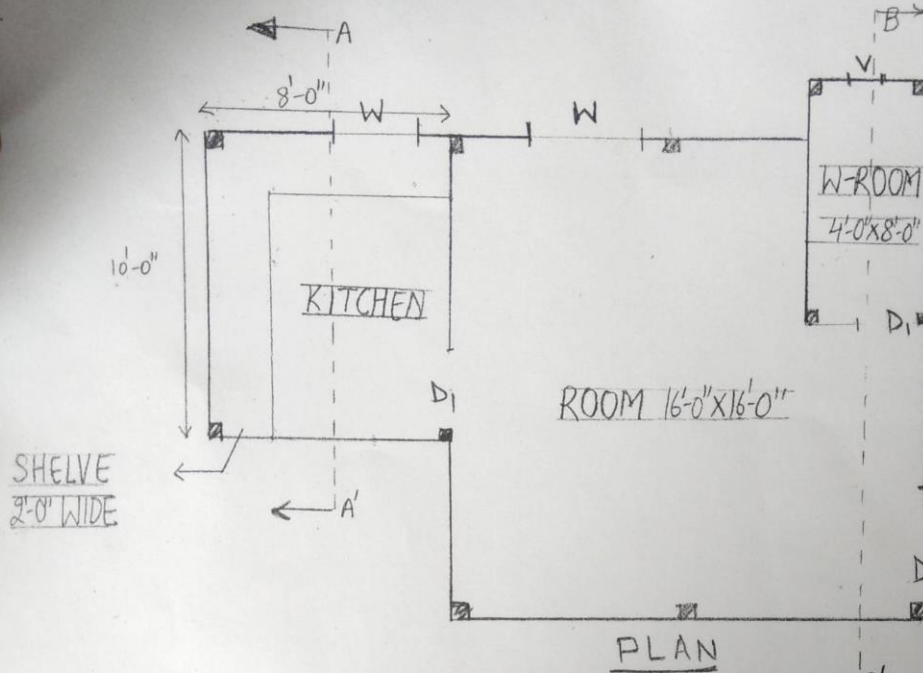



SECTIONAL VIEW AA'

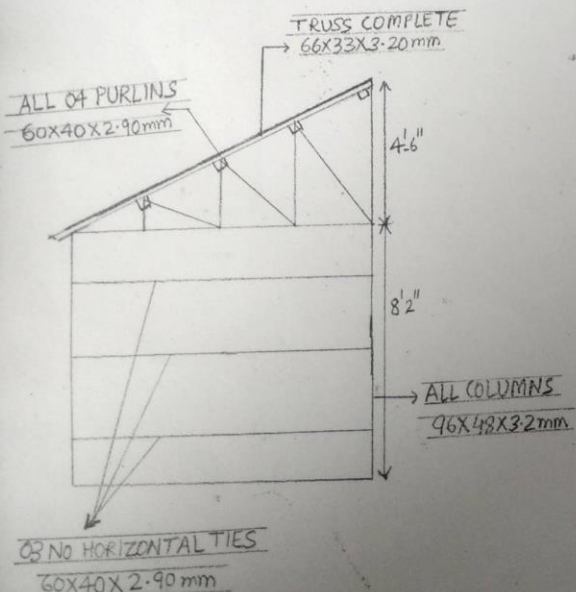

X-SECTION AT A-A'

- D- 3'-3" X 7'-0"
- D1- 2'-6" X 7'-0"
- W- 3'-0" X 3'-0"
- V- 2'-0" X 1'-6"


SECTIONAL VIEW BB'

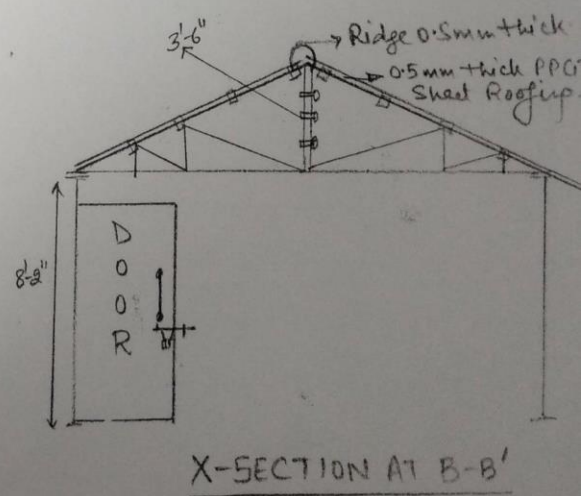

*Signature*  
(JL)




S No 5th

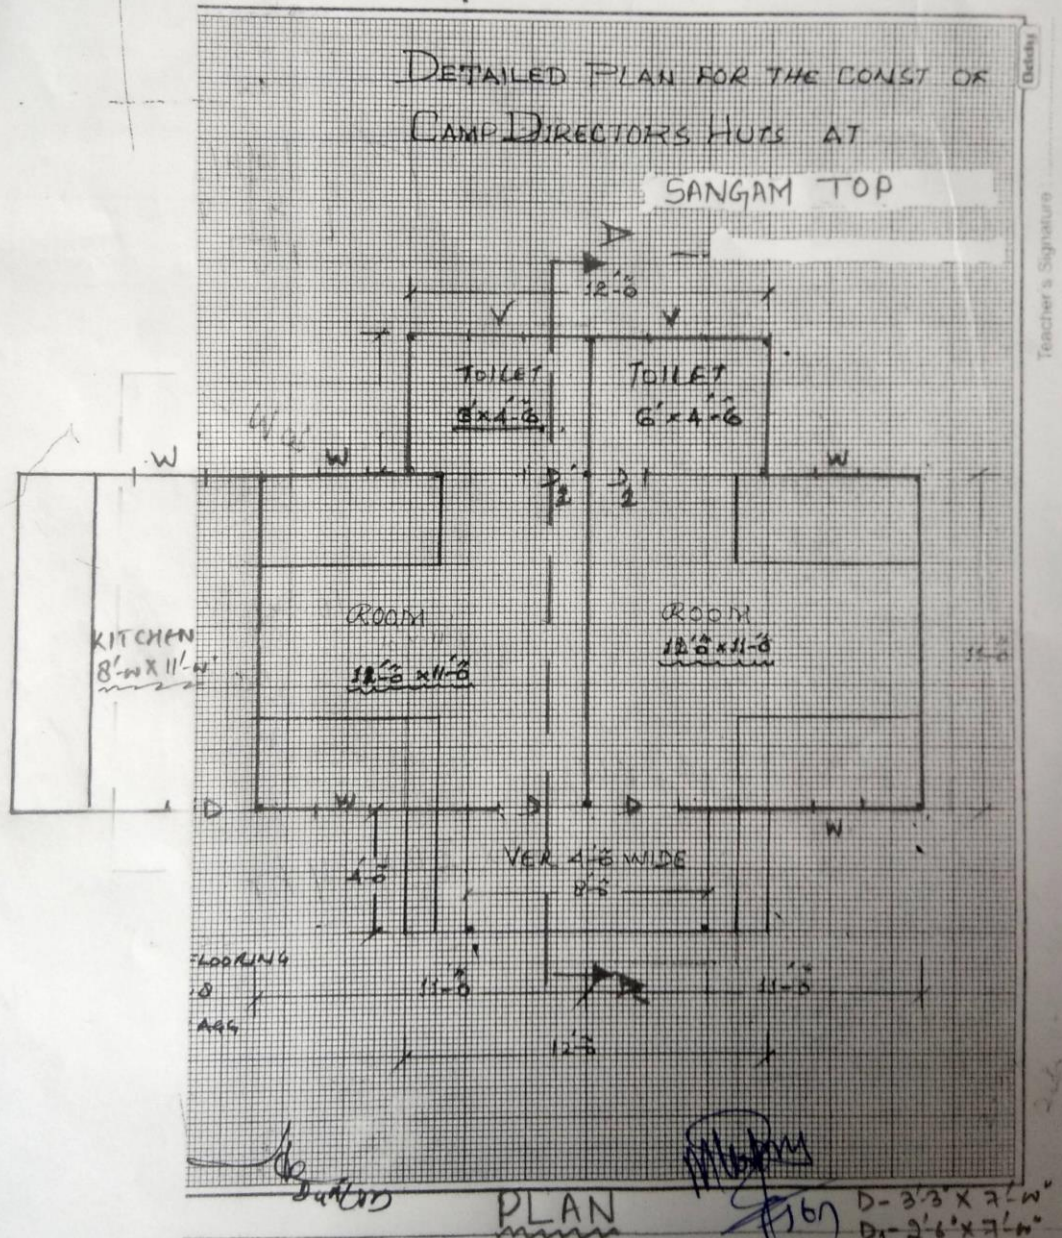

Page 3 of 12

D-3'3" x 7'6"  
D<sub>1</sub>-2'6" x 7'6"  
W-3'6" x 3'6"  
V-2'6" x 1'6"  
KTO

# CONST OF CAMP DIRECTOR HUTS AT SANGAM TOP

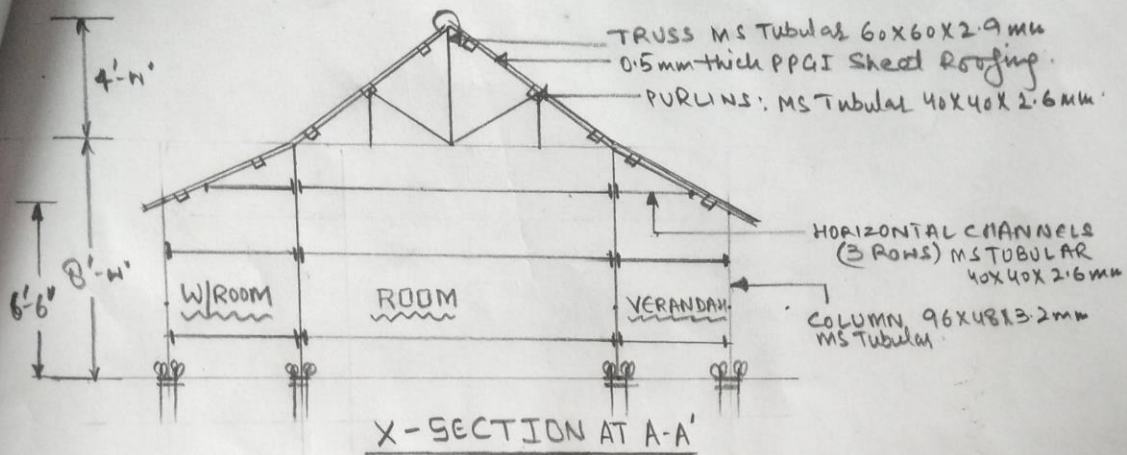

*Maipras*  
 (S62)


Page 2 of 2

*Devi (M)*




# DRAWING S.No 6th HEL-SERVICES SHED AT SANGAM & LOWER HOLY CAVE

MAP NOT-TO-SCALE

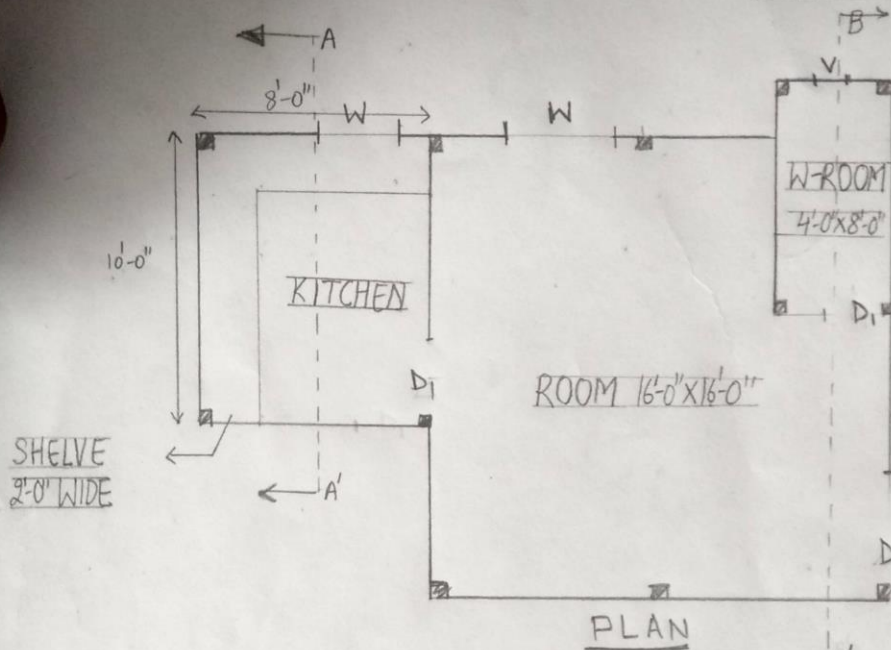



## SECTIONAL VIEW AA'

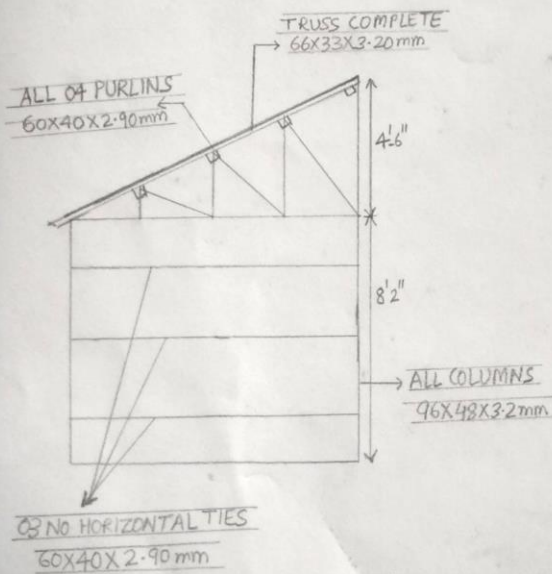

## X-SECTION AT A-A'

- D- 3'-3" X 7'-0"
- DI- 2'-6" X 7'-0"
- N- 3'-0" X 3'-0"
- V- 2'-0" X 1'-6"


## SECTIONAL VIEW BB'

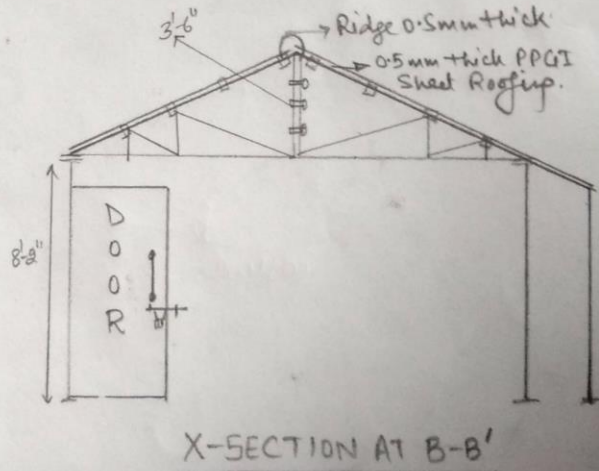



S.No 7/A)

**DETAILED PLAN FOR THE CONSTRUCTION OF OFFICE CUM RESIDENTIAL HUT FOR SERVICE PROVIDERS FOR ISSUANCE OF SMART CARDS (TRACKING) TO YATRIES AT LOWER HOLYCAVE**

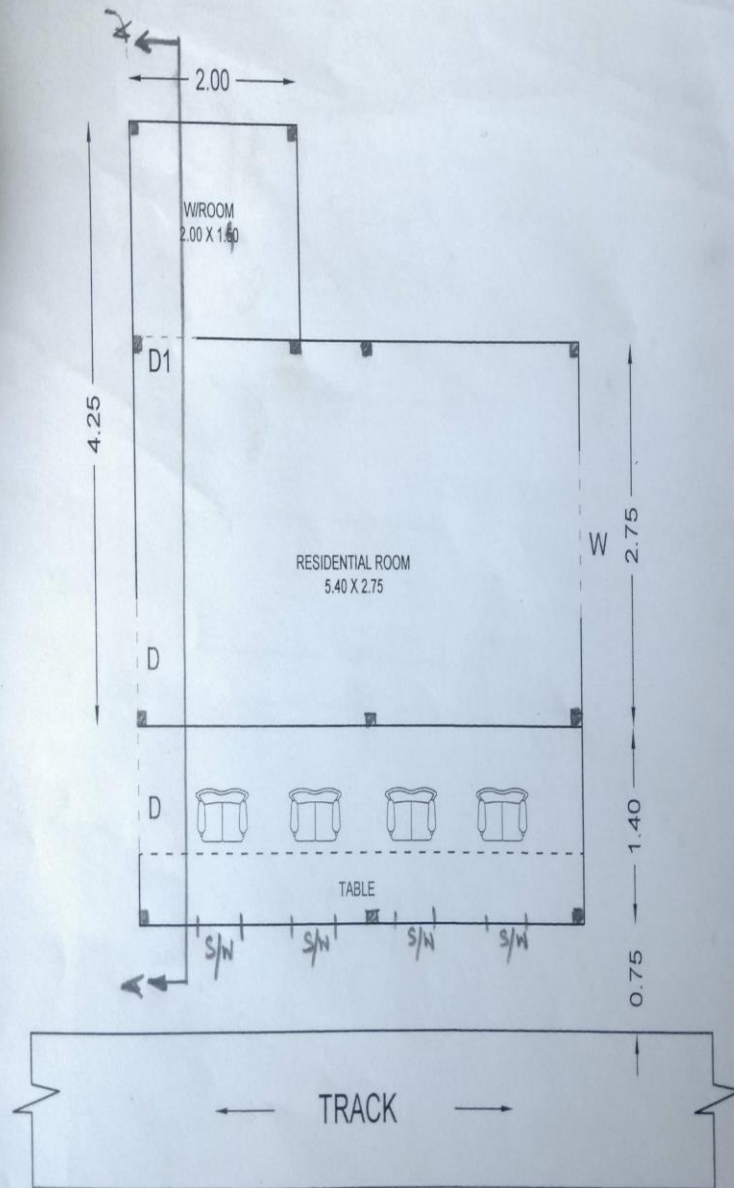

*[Signature]*  
JE

*[Signature]*  
(BARTAL)

QM(water)


ALL DIMENSIONS ARE IN METERS

D	= 0.90 X 2.10
D1	= 0.75 X 2.10


Scanned by TapScanner

Page No 1 of 2

# SMART CARD SERVICE PROVIDERS AT LOWER HOLYCAVE

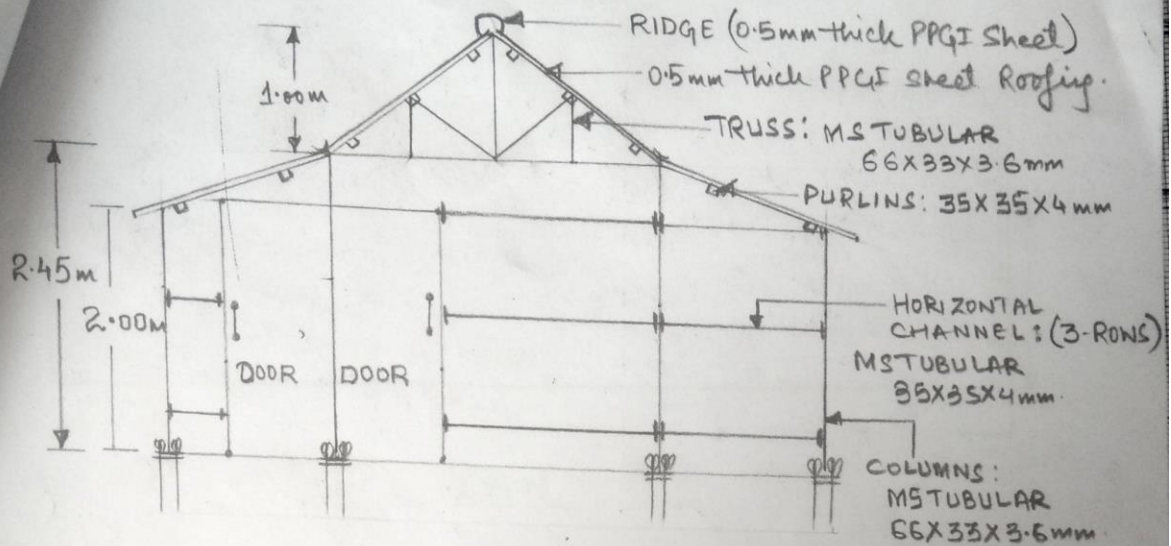

X-SECTION AT A-A'

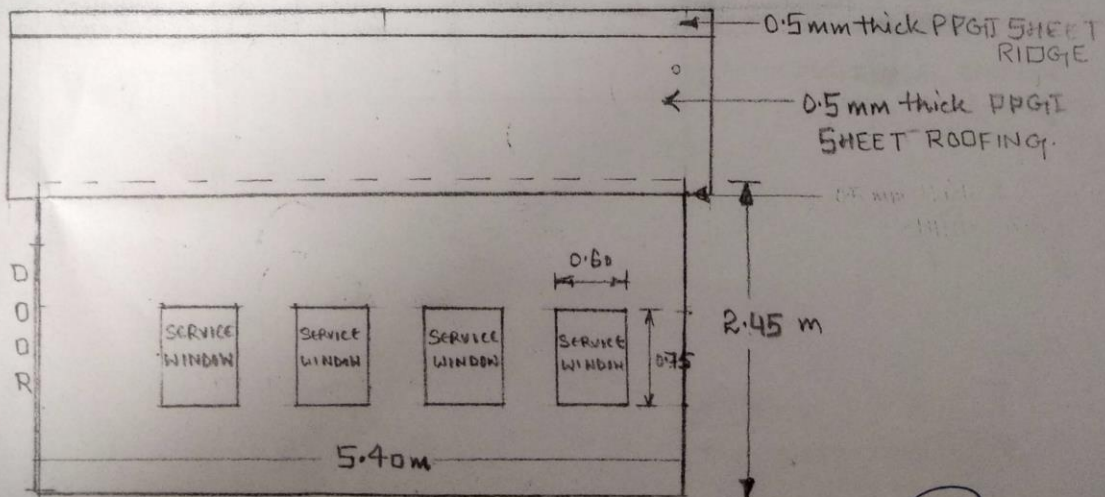

FRONT ELEVATION


Page No 2 of 02

Scanned by TapScanner


S.No 7 (B)

# CONSTRUCTION OF SUPER-STRUCTURE FOR SADHUSHED AT HOLYCAVE

SCALE 1CM=2FT OR 1:60

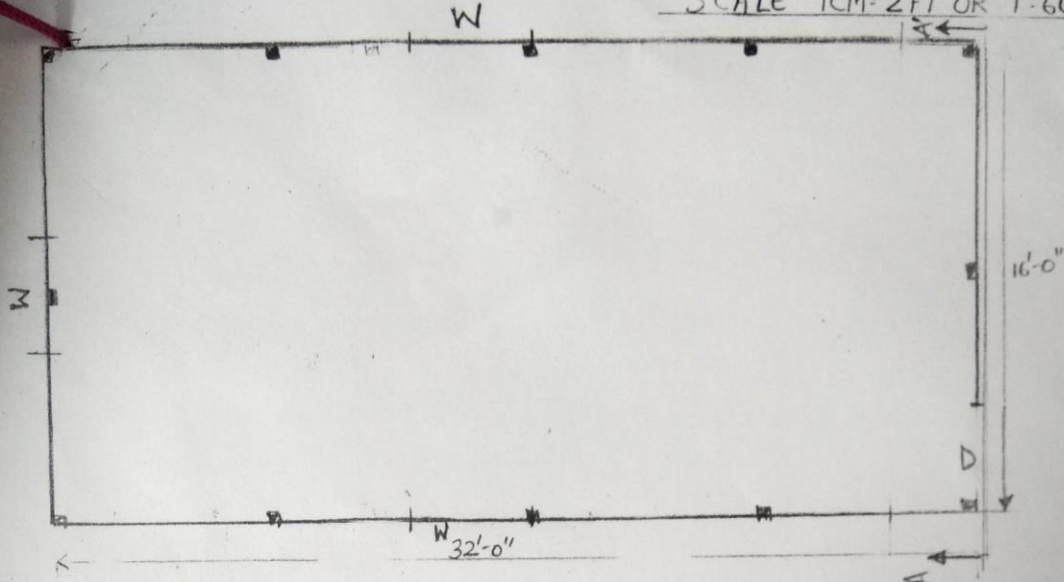

PLAN

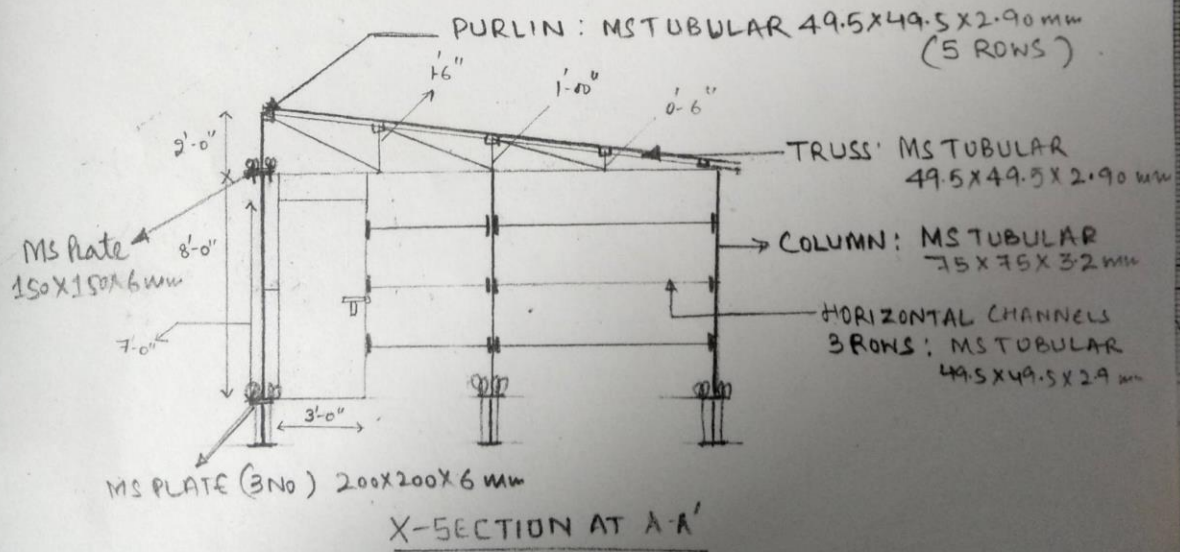

X-SECTION AT A-A'

*Signature*  
(Sd/-)

*Signature*  
Date 4/11/17

(D) DOOR - 3'-3" X 7'-0"

(W) WINDOW - 3'-0" X 3'-0"
